Malpas and Birmingham Inc.
962 Chula Vista Ave.
Burlingame CA 94010

55 Sheridan St - Dunham Kawano
Construction Schedule
Completed Tasks in Grey,
Architect/Client Tasks in Geen
Current Changes in Blue

Issued: May 23, 2006
September 16, 2006
October 2, 2006
February 6, 2007
April 17, 2007

ID	Task Name	Duration	Start	Finish
1	Start	0 days	Fri 10/14/05	Fri 10/14/05
2	Demo Brick Bldg	1 day	Fri 10/14/05	Fri 10/14/05
3	Soil Injection	2 wks	Tue 11/15/05	Mon 11/28/05
4	Neighbor Wall	2 wks	Fri 3/3/06	Thu 3/16/06
5	Excavation	1 day	Mon 3/20/06	Mon 3/20/06
6	Garden Demo/Remove Dirt	1 wk	Tue 5/1/07	Mon 5/7/07
7	Garden Underslab Utilities	1 wk	Tue 5/8/07	Mon 5/14/07
8	Garden Concrete	1 wk	Tue 5/15/07	Mon 5/21/07
9	Garden Structures	2 wks	Tue 5/22/07	Mon 6/4/07
10	Garden Planting	2 wks	Mon 4/2/07	Fri 4/13/07
11	Underslab Utilities	2 days	Tue 3/21/06	Wed 3/22/06
12	Underslab Inspection	0 days	Mon 3/27/06	Mon 3/27/06
13	Rebar	1 wk	Mon 3/27/06	Fri 3/31/06
14	Structural Concrete	1 day	Thu 4/20/06	Thu 4/20/06
15	Shotcrete Garden Wall	1 day	Thu 5/11/06	Thu 5/11/06
16	Topping Slab 1st	4 days	Tue 5/22/07	Fri 5/25/07
17	Conc Over Pan Deck 2,3,4	3 days	Thu 8/24/06	Mon 8/28/06
18	Conc Sidewalk	1 wk	Mon 6/25/07	Fri 6/29/07
19	Struc Steel Shops	2 wks	Mon 4/3/06	Fri 4/14/06
20	Struc Steel Fabricate	2 wks	Mon 4/17/06	Fri 4/28/06
21	Struc Steel Erect Rear	4 wks	Mon 5/8/06	Fri 6/2/06
22	Struct Steel Erect Front	2 wks	Mon 6/19/06	Fri 6/30/06
23	Stair Shops	2 wks	Mon 5/8/06	Fri 5/19/06
24	Stair Fabricate	2 wks	Mon 5/22/06	Fri 6/2/06
25	Stair Erect	2 wks	Mon 6/5/06	Fri 6/16/06
26	Pan Deck	2 wks	Mon 6/5/06	Fri 6/16/06
27	API Shops	6 wks	Mon 5/8/06	Fri 6/16/06
28	API Fabricate	12 wks	Mon 5/8/06	Fri 7/28/06
29	API Install	6 wks	Tue 8/29/06	Mon 10/9/06
30	Roof Carpentry	3 wks	Tue 8/29/06	Mon 9/18/06
31	Finish Carp Design	0 days	Tue 7/10/07	Tue 7/10/07
32	Finish Carpentry	6 wks	Tue 7/10/07	Mon 8/20/07
33	Final Casework Design - Check	0 days	Wed 2/7/07	Wed 2/7/07
34	Casework Field Measure - Sche	3 wks	Wed 2/7/07	Tue 2/27/07
35	Casework Shops	1 wk	Tue 4/10/07	Mon 4/16/07
36	Casework Fabricate	8 wks	Tue 4/17/07	Mon 6/11/07
37	Casework Install	2 wks	Tue 6/12/07	Mon 6/25/07
38	Insulation	2 wks	Tue 2/27/07	Mon 3/12/07

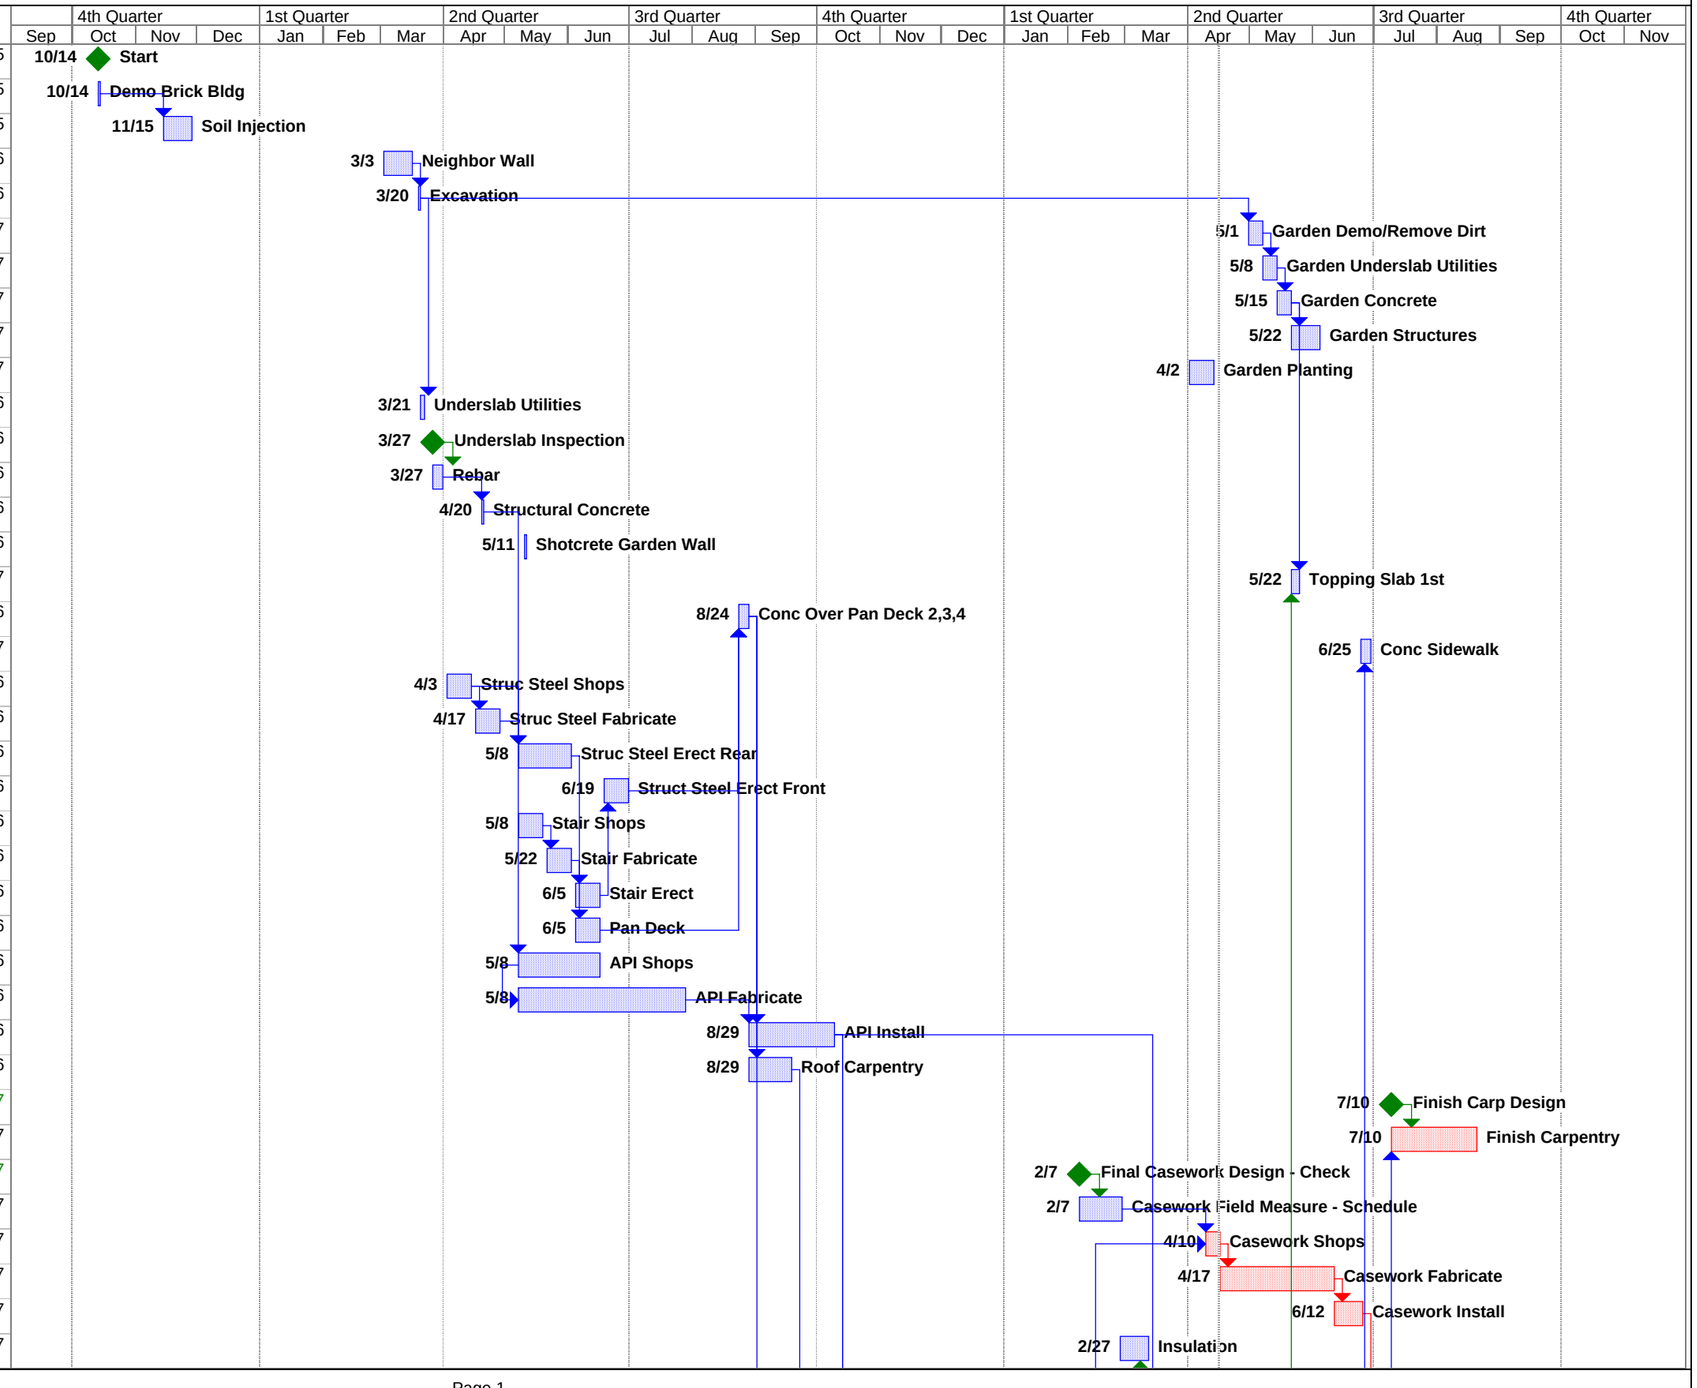

Malpas and Birmingham Inc.
962 Chula Vista Ave.
Burlingame CA 94010

55 Sheridan St - Dunham Kawano
Construction Schedule
Completed Tasks in Grey,
Architect/Client Tasks in Geen
Current Changes in Blue

Issued: May 23, 2006
September 16, 2006
October 2, 2006
February 6, 2007
April 17, 2007

ID	Task Name	Duration	Start	Finish
39	Roofing	1 wk	Tue 9/19/06	Mon 9/25/06
40	Storefront Shops	2 wks	Mon 6/12/06	Fri 6/23/06
41	Operable Sash Fabricate	8 wks	Mon 6/26/06	Fri 8/18/06
42	Storefront Fabricate	8 wks	Mon 6/26/06	Fri 8/18/06
43	Storefront Install	4 wks	Thu 3/15/07	Wed 4/11/07
44	Ext Door Design	0 days	Thu 8/10/06	Thu 8/10/06
45	Ext Door Fabricate	4 wks	Tue 10/10/06	Mon 11/6/06
46	Int Door Design	0 days	Thu 10/12/06	Thu 10/12/06
47	Int Door Order	3 wks	Tue 1/30/07	Mon 2/19/07
48	Int Door Install	2 wks	Tue 3/6/07	Mon 3/19/07
49	Exterior Gyp Bd	1 wk	Mon 2/12/07	Fri 2/16/07
50	Exterior Lath/Waterproofing	1 wk	Mon 2/19/07	Fri 2/23/07
51	Stucco samples, color approval	0 days	Tue 4/17/07	Tue 4/17/07
52	Stucco Scratch & Brown	4 wks	Tue 4/17/07	Mon 5/14/07
53	Stucco Color Coat	2 wks	Mon 5/22/06	Fri 6/2/06
54	Lt Ga Framing	12 wks	Tue 8/29/06	Mon 11/20/06
55	Cover-Up Inspection	0 days	Mon 2/26/07	Mon 2/26/07
56	Drywall	9 wks	Mon 2/19/07	Fri 4/20/07
57	Roof Paver Order	4 wks	Tue 5/1/07	Mon 5/28/07
58	Roof Paver Stock	1 wk	Tue 5/29/07	Mon 6/4/07
59	Roof Paver Install	2 wks	Tue 6/5/07	Mon 6/18/07
60	Final Stone & Tile Selection	0 days	Thu 3/15/07	Thu 3/15/07
61	Stone Tub Deck Fabricate	2 wks	Tue 5/1/07	Mon 5/14/07
62	Stone Tub Deck Install	4 days	Tue 5/15/07	Fri 5/18/07
63	Stone Counter Fabricate	4 wks	Tue 6/26/07	Mon 7/23/07
64	Stone Counter Install	1 wk	Tue 7/24/07	Mon 7/30/07
65	Stone Tile Order	2 wks	Thu 3/15/07	Wed 3/28/07
66	Stone Tile Install	3 wks	Thu 3/29/07	Wed 4/18/07
67	Glass Tile Order	12 wks	Wed 3/21/07	Tue 6/12/07
68	Glass Tile Install	4 days	Wed 6/13/07	Mon 6/18/07
69	Final Flooring Selection	0 days	Wed 10/18/06	Wed 10/18/06
70	Wood Flooring	3 wks	Mon 6/18/07	Fri 7/6/07
71	Final Paint Selection	0 days	Thu 4/12/07	Thu 4/12/07
72	Paint Ext Steel	2 wks	Tue 10/10/06	Mon 10/23/06
73	Paint Int Steel	2 wks	Mon 4/23/07	Fri 5/4/07
74	Paint Walls/Ceilings	8 wks	Mon 4/23/07	Fri 6/15/07
75	Install Appliances	1 wk	Tue 7/31/07	Mon 8/6/07
76	Spray Booth Decision	7 mons	Tue 7/4/06	Mon 1/15/07

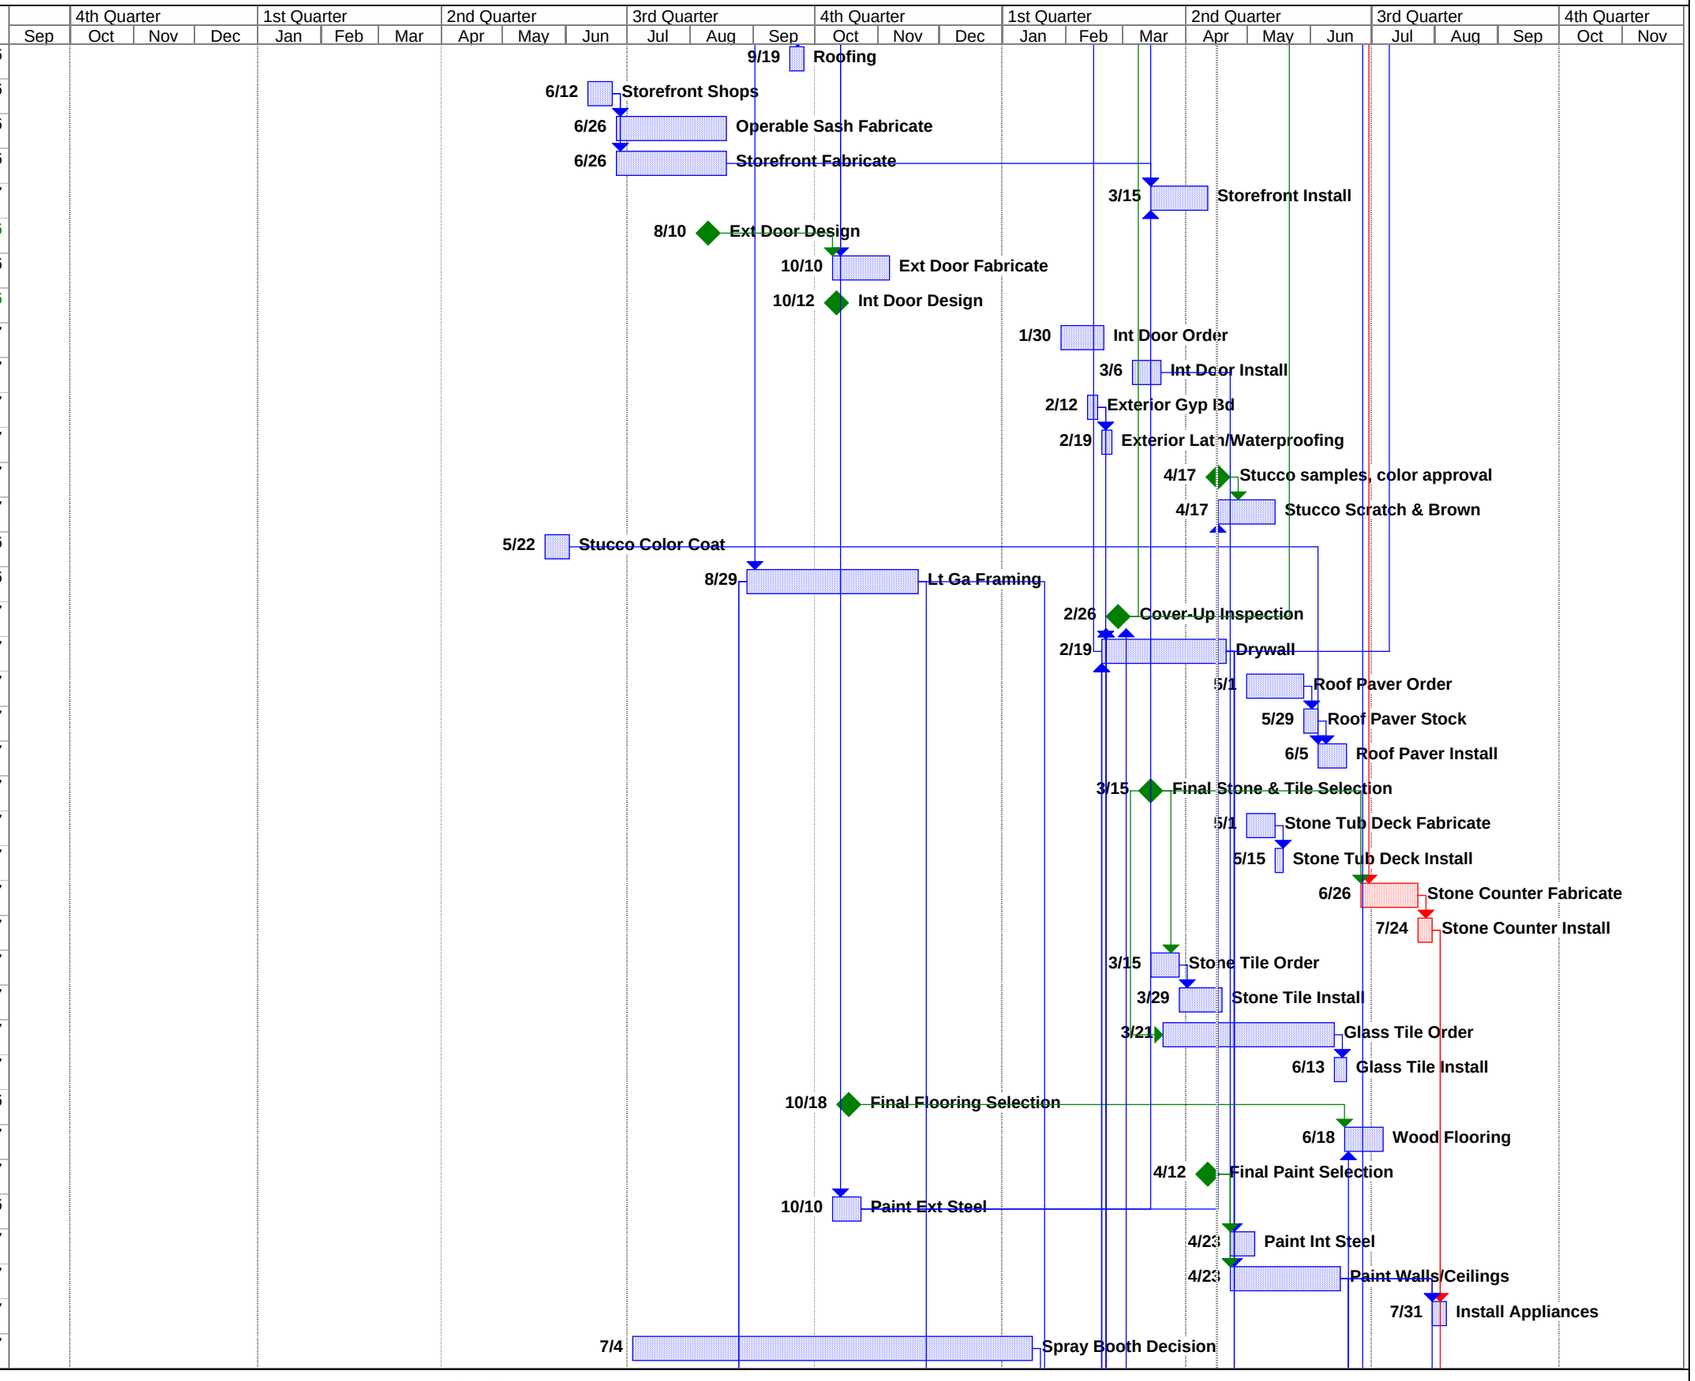

Malpas and Birmingham Inc.
962 Chula Vista Ave.
Burlingame CA 94010

55 Sheridan St - Dunham Kawano
Construction Schedule
Completed Tasks in Grey,
Architect/Client Tasks in Geen
Current Changes in Blue

Issued: May 23, 2006
September 16, 2006
October 2, 2006
February 6, 2007
April 17, 2007
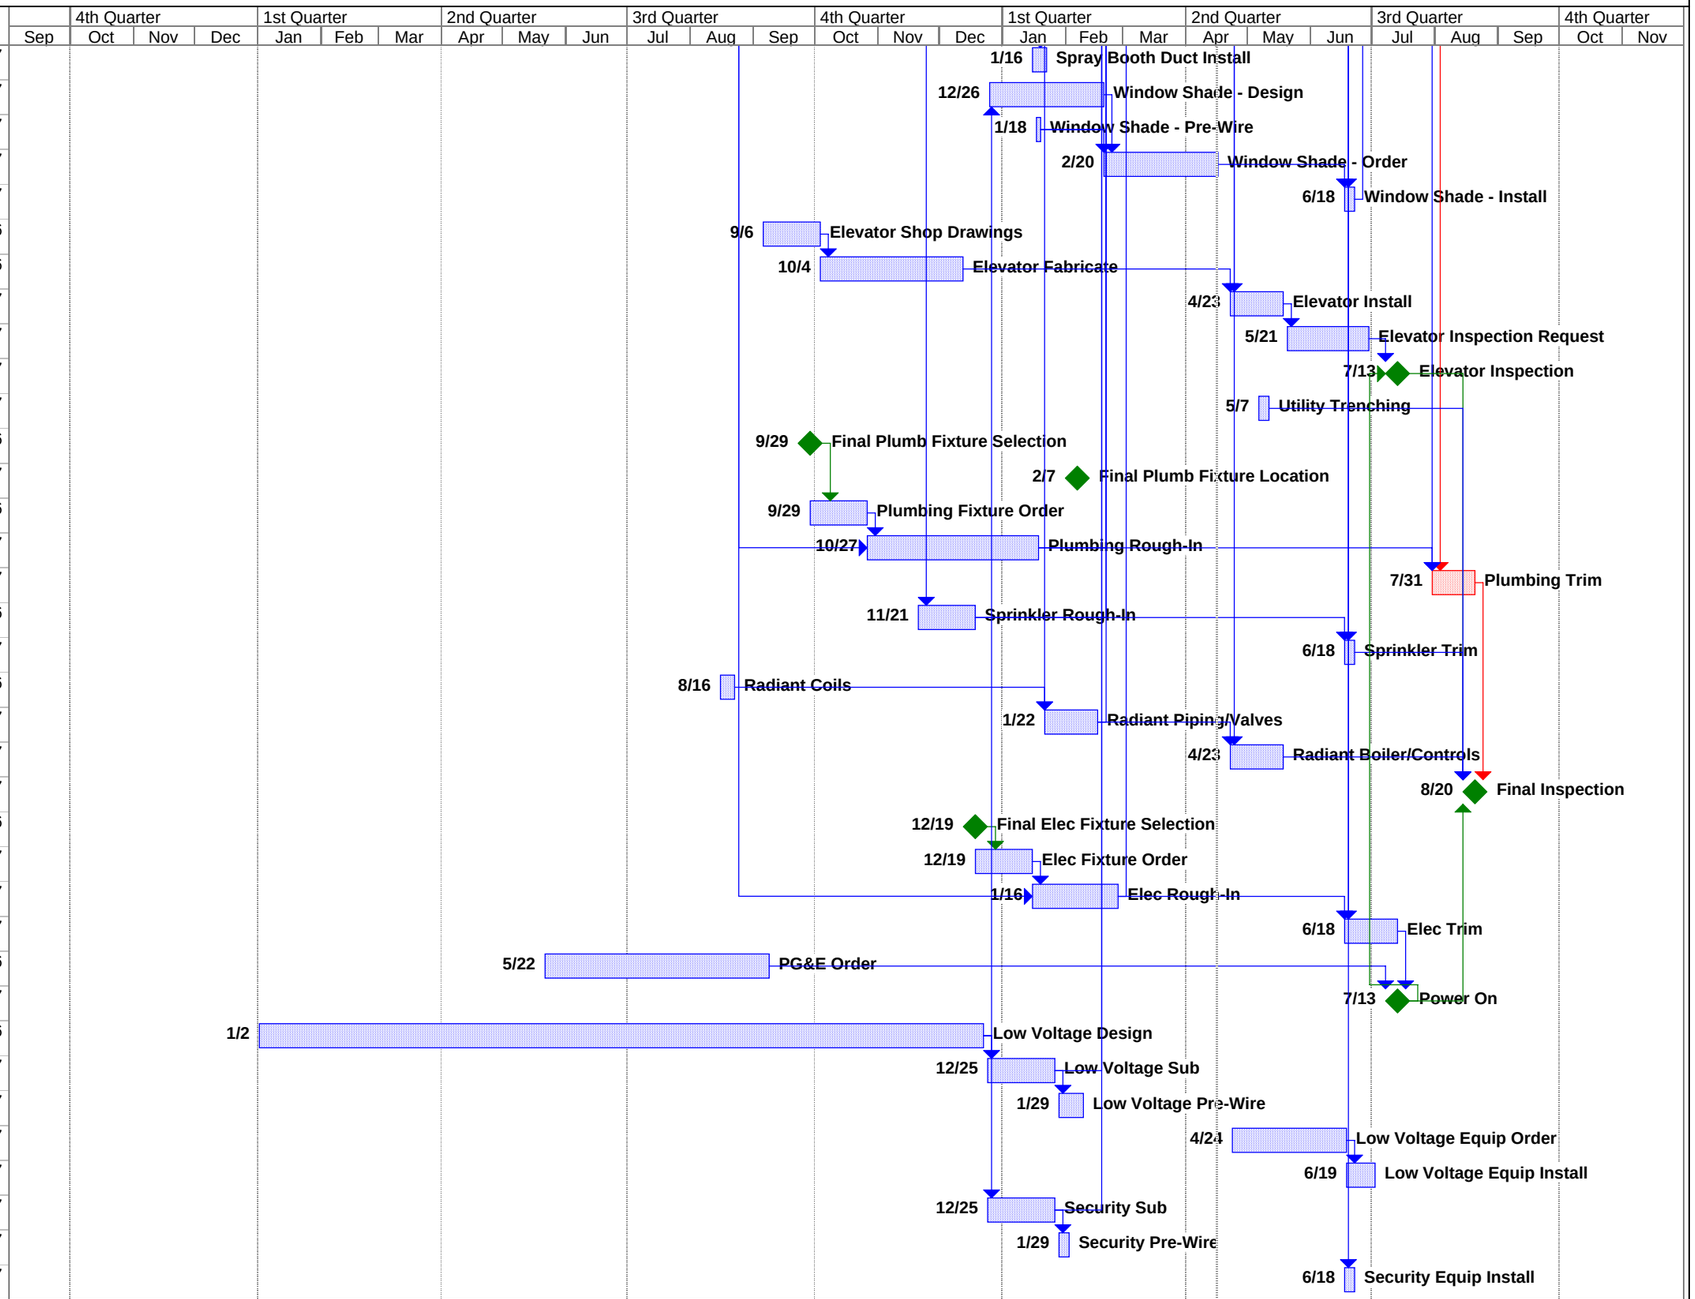
ID	Task Name	Duration	Start	Finish
77	Spray Booth Duct Install	1 wk	Tue 1/16/07	Mon 1/22/07
78	Window Shade - Design	2 mons	Tue 12/26/06	Mon 2/19/07
79	Window Shade - Pre-Wire	2 days	Thu 1/18/07	Fri 1/19/07
80	Window Shade - Order	8 wks	Tue 2/20/07	Mon 4/16/07
81	Window Shade - Install	1 wk	Mon 6/18/07	Fri 6/22/07
82	Elevator Shop Drawings	4 wks	Wed 9/6/06	Tue 10/3/06
83	Elevator Fabricate	10 wks	Wed 10/4/06	Tue 12/12/06
84	Elevator Install	4 wks	Mon 4/23/07	Fri 5/18/07
85	Elevator Inspection Request	6 wks	Mon 5/21/07	Fri 6/29/07
86	Elevator Inspection	0 days	Fri 7/13/07	Fri 7/13/07
87	Utility Trenching	1 wk	Mon 5/7/07	Fri 5/11/07
88	Final Plumb Fixture Selection	0 days	Fri 9/29/06	Fri 9/29/06
89	Final Plumb Fixture Location	0 days	Wed 2/7/07	Wed 2/7/07
90	Plumbing Fixture Order	4 wks	Fri 9/29/06	Thu 10/26/06
91	Plumbing Rough-In	12 wks	Fri 10/27/06	Thu 1/18/07
92	Plumbing Trim	3 wks	Tue 7/31/07	Mon 8/20/07
93	Sprinkler Rough-In	4 wks	Tue 11/21/06	Mon 12/18/06
94	Sprinkler Trim	1 wk	Mon 6/18/07	Fri 6/22/07
95	Radiant Coils	1 wk	Wed 8/16/06	Tue 8/22/06
96	Radiant Piping/Valves	4 wks	Mon 1/22/07	Fri 2/16/07
97	Radiant Boiler/Controls	4 wks	Mon 4/23/07	Fri 5/18/07
98	Final Inspection	0 days	Mon 8/20/07	Mon 8/20/07
99	Final Elec Fixture Selection	0 days	Tue 12/19/06	Tue 12/19/06
100	Elec Fixture Order	4 wks	Tue 12/19/06	Mon 1/15/07
101	Elec Rough-In	6 wks	Tue 1/16/07	Mon 2/26/07
102	Elec Trim	4 wks	Mon 6/18/07	Fri 7/13/07
103	PG&E Order	16 wks	Mon 5/22/06	Fri 9/8/06
104	Power On	0 days	Fri 7/13/07	Fri 7/13/07
105	Low Voltage Design	51 wks	Mon 1/2/06	Fri 12/22/06
106	Low Voltage Sub	5 wks	Mon 12/25/06	Fri 1/26/07
107	Low Voltage Pre-Wire	2 wks	Mon 1/29/07	Fri 2/9/07
108	Low Voltage Equip Order	8 wks	Tue 4/24/07	Mon 6/18/07
109	Low Voltage Equip Install	2 wks	Tue 6/19/07	Mon 7/2/07
110	Security Sub	5 wks	Mon 12/25/06	Fri 1/26/07
111	Security Pre-Wire	1 wk	Mon 1/29/07	Fri 2/2/07
112	Security Equip Install	1 wk	Mon 6/18/07	Fri 6/22/07
